

STATINTL


To:

Oct. 13, 1959

From: Clarence L. Johnson

Subject: PROJECT MEMO - PRODUCTION SCHEDULE, A-12

Because of engine changes and configuration problems, the first flight will be 20 months from go-ahead. All 12 airplanes will, however, be done in 36 months.

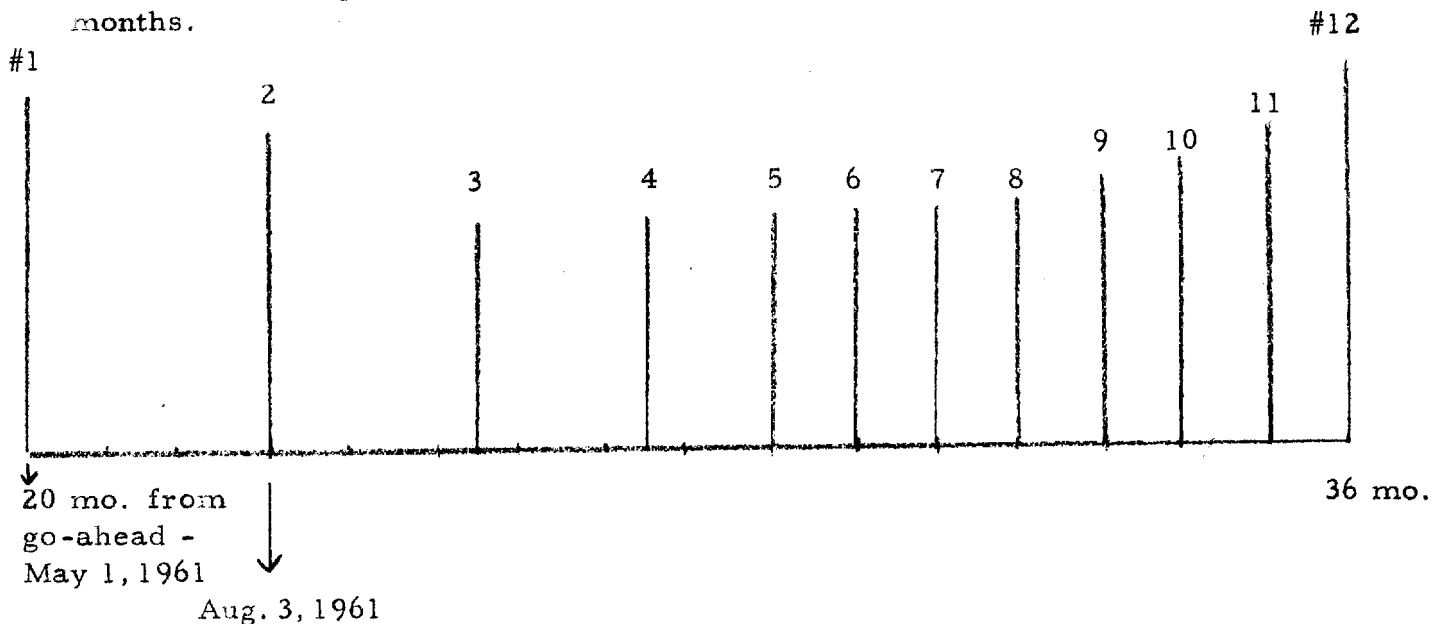


STATINTL Delivery to Customer at [REDACTED]

STATINTL Have to deliver aircraft to [REDACTED] approximately one month prior to above dates to provide time for re-assembly and production test.

#1	May 1, 1961	#5	Feb. 7, 1962	#9	June 13, 1962
#2	Aug. 3, 1961	#6	Mar. 7, 1962	#10	July 11, 1962
#3	Oct. 18, 1961	#7	Apr. 11, 1962	#11	Aug. 10, 1962
#4	Dec. 20, 1961	#8	May 11, 1962	#12	Sept. 5, 1962

STATINTL

[REDACTED]  
Clarence L. Johnson  
Vice President  
Advanced Development Projects

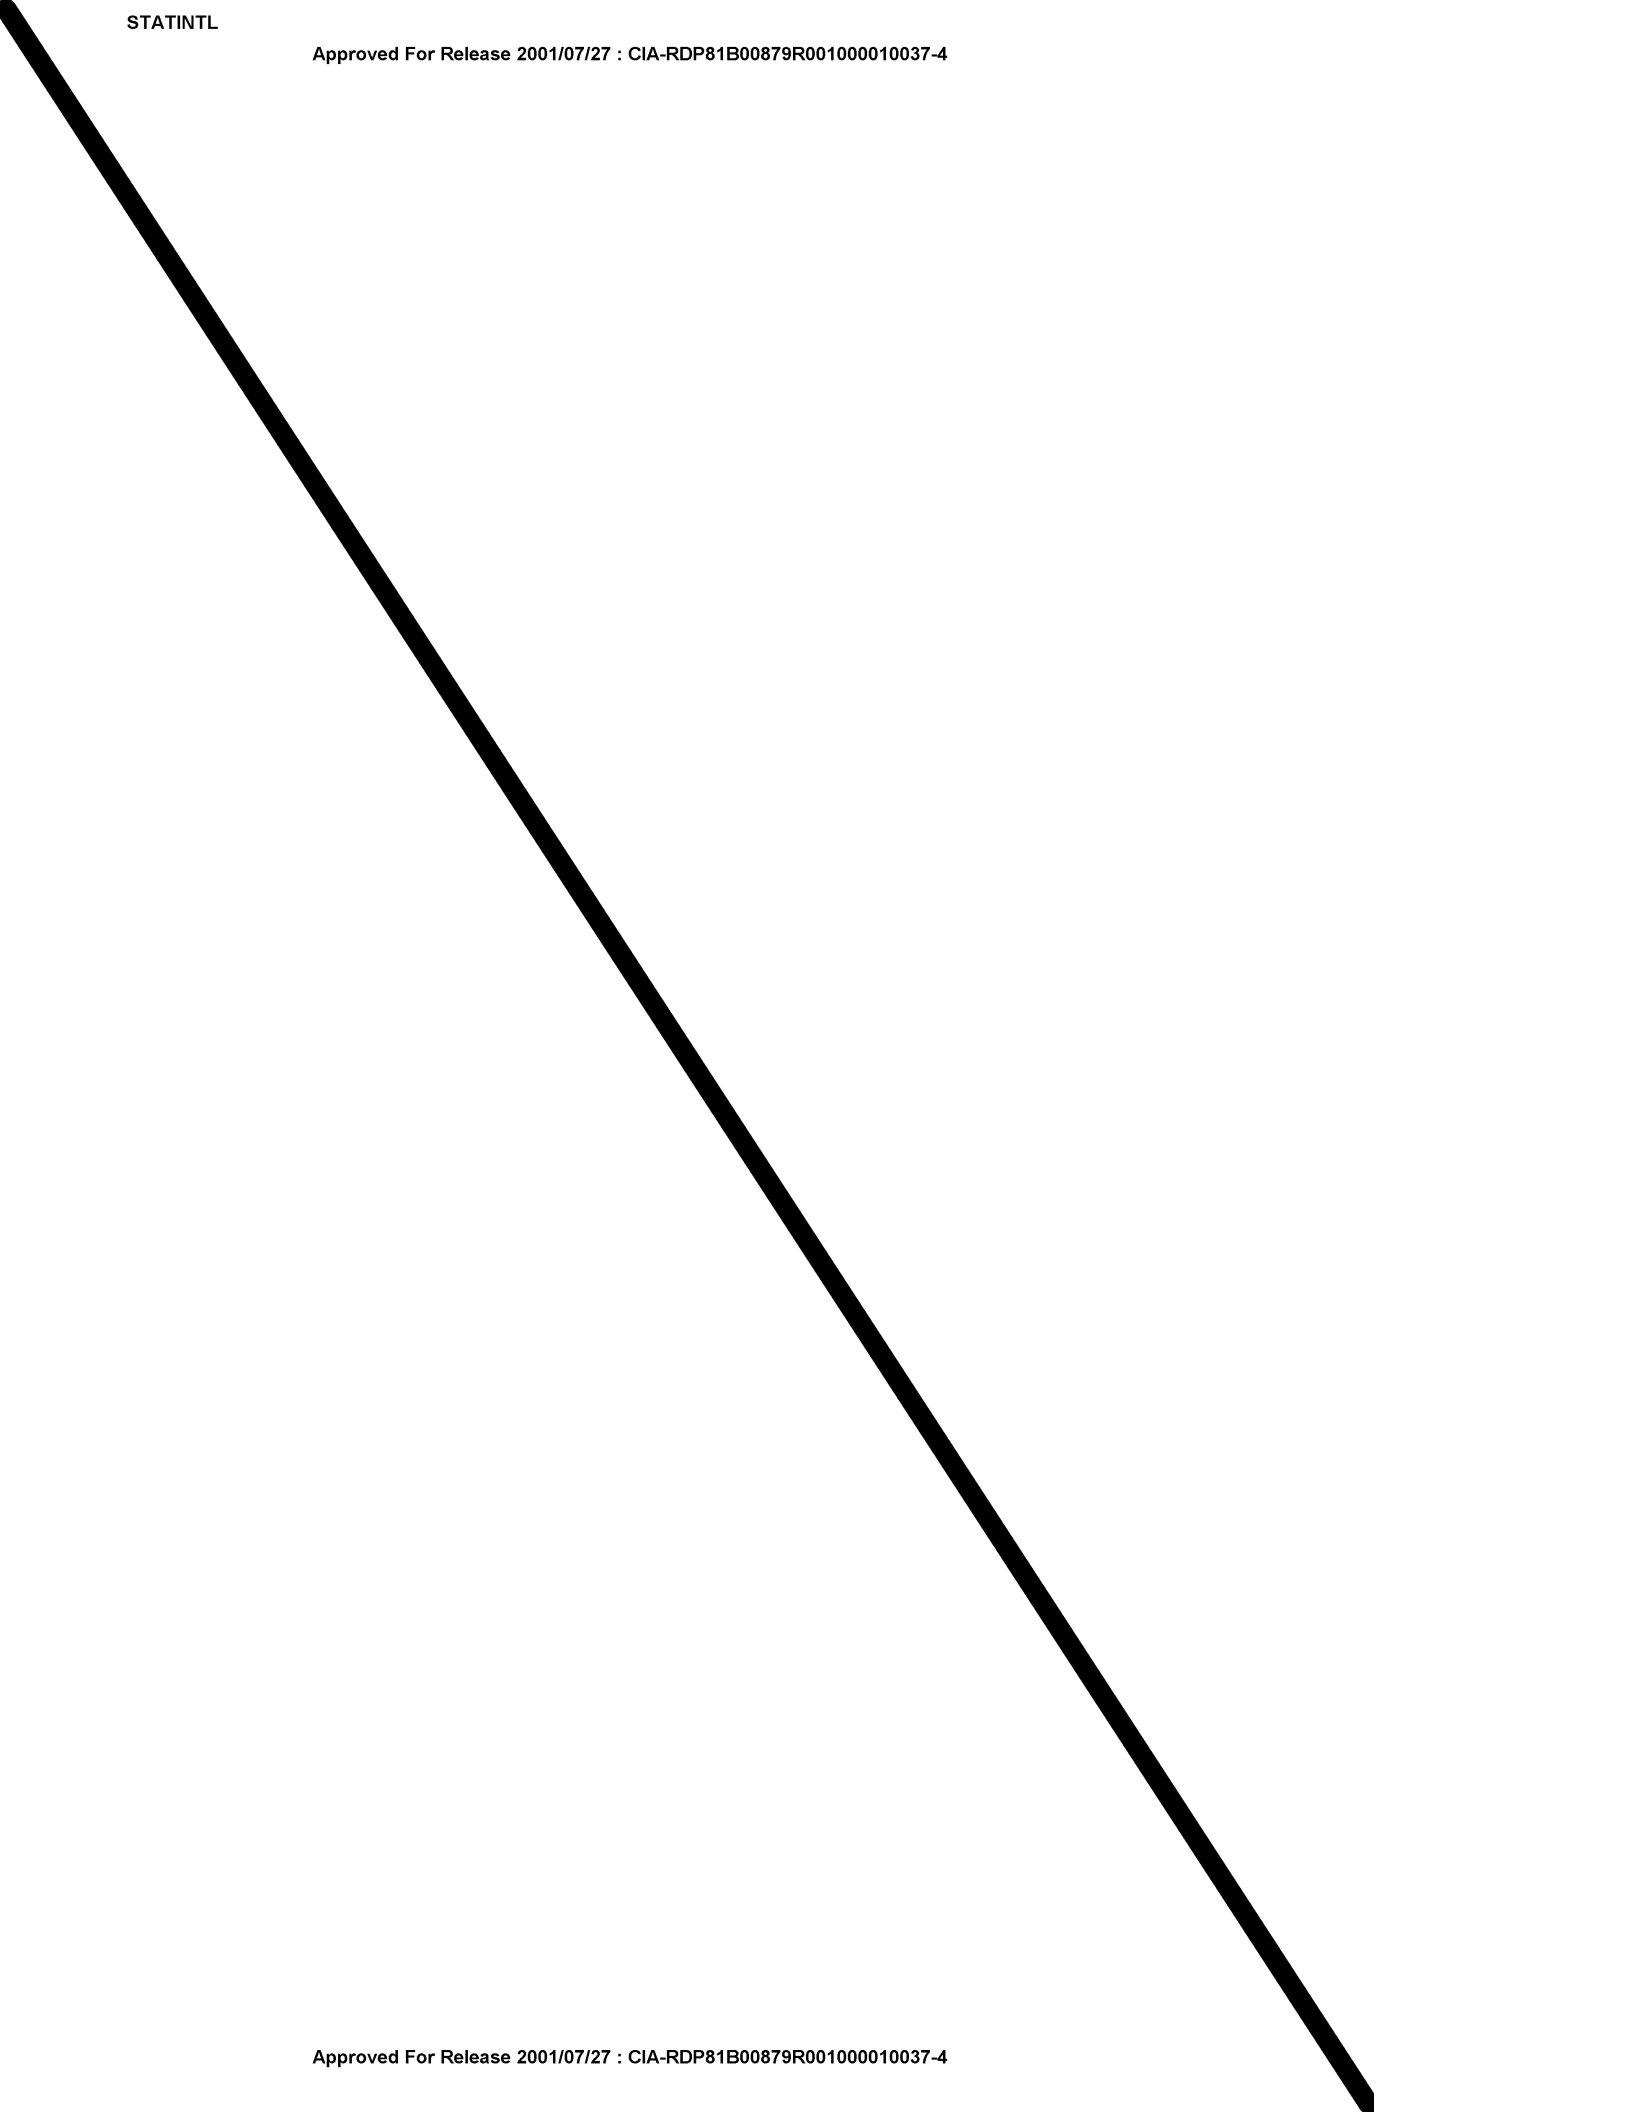

# ADVANCED DEVELOPMENT PROJECTS ORGANIZATION CHART

SEPT. 21, 1959

**C.L. JOHNSON**  
VICE PRESIDENT  
ADVANCED DEVELOPMENT PROJECTS

STATINTL

INSPECTION

STAFF ASST.

STATINTL

FINANCE

CONTRACTS

STATINTL

STATINTL

ENGINEERING

A-12

ENGINEERING

U-2

ASST.

FLIGHT TEST

ASST.

ELECTRONICS

MANUFACTURING &  
FIELD SERVICE

ASST. R.G. PLUE


STATINTL

STATINTL

STATINTL

## ORGANIZATION CHART

SEPT. 21, 1959

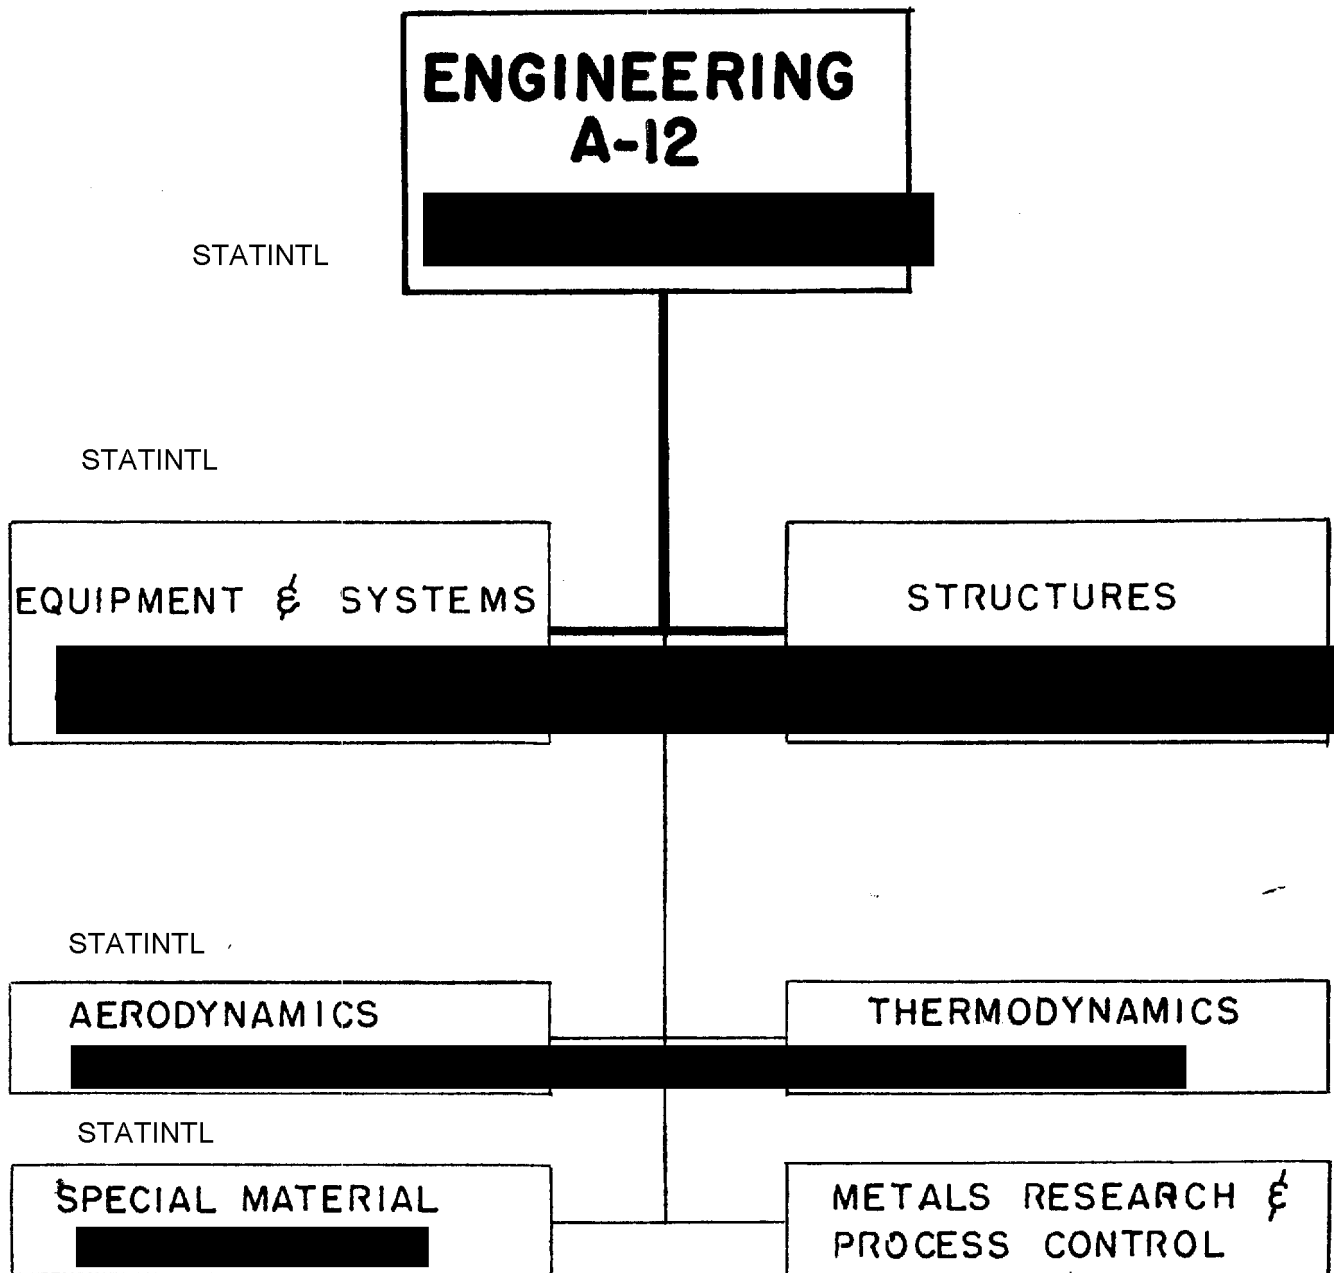


STATINTL

Clarence L. Johnson  
Vice President

Advanced Development Projects

## ORGANIZATION CHART

SEPT. 21, 1959

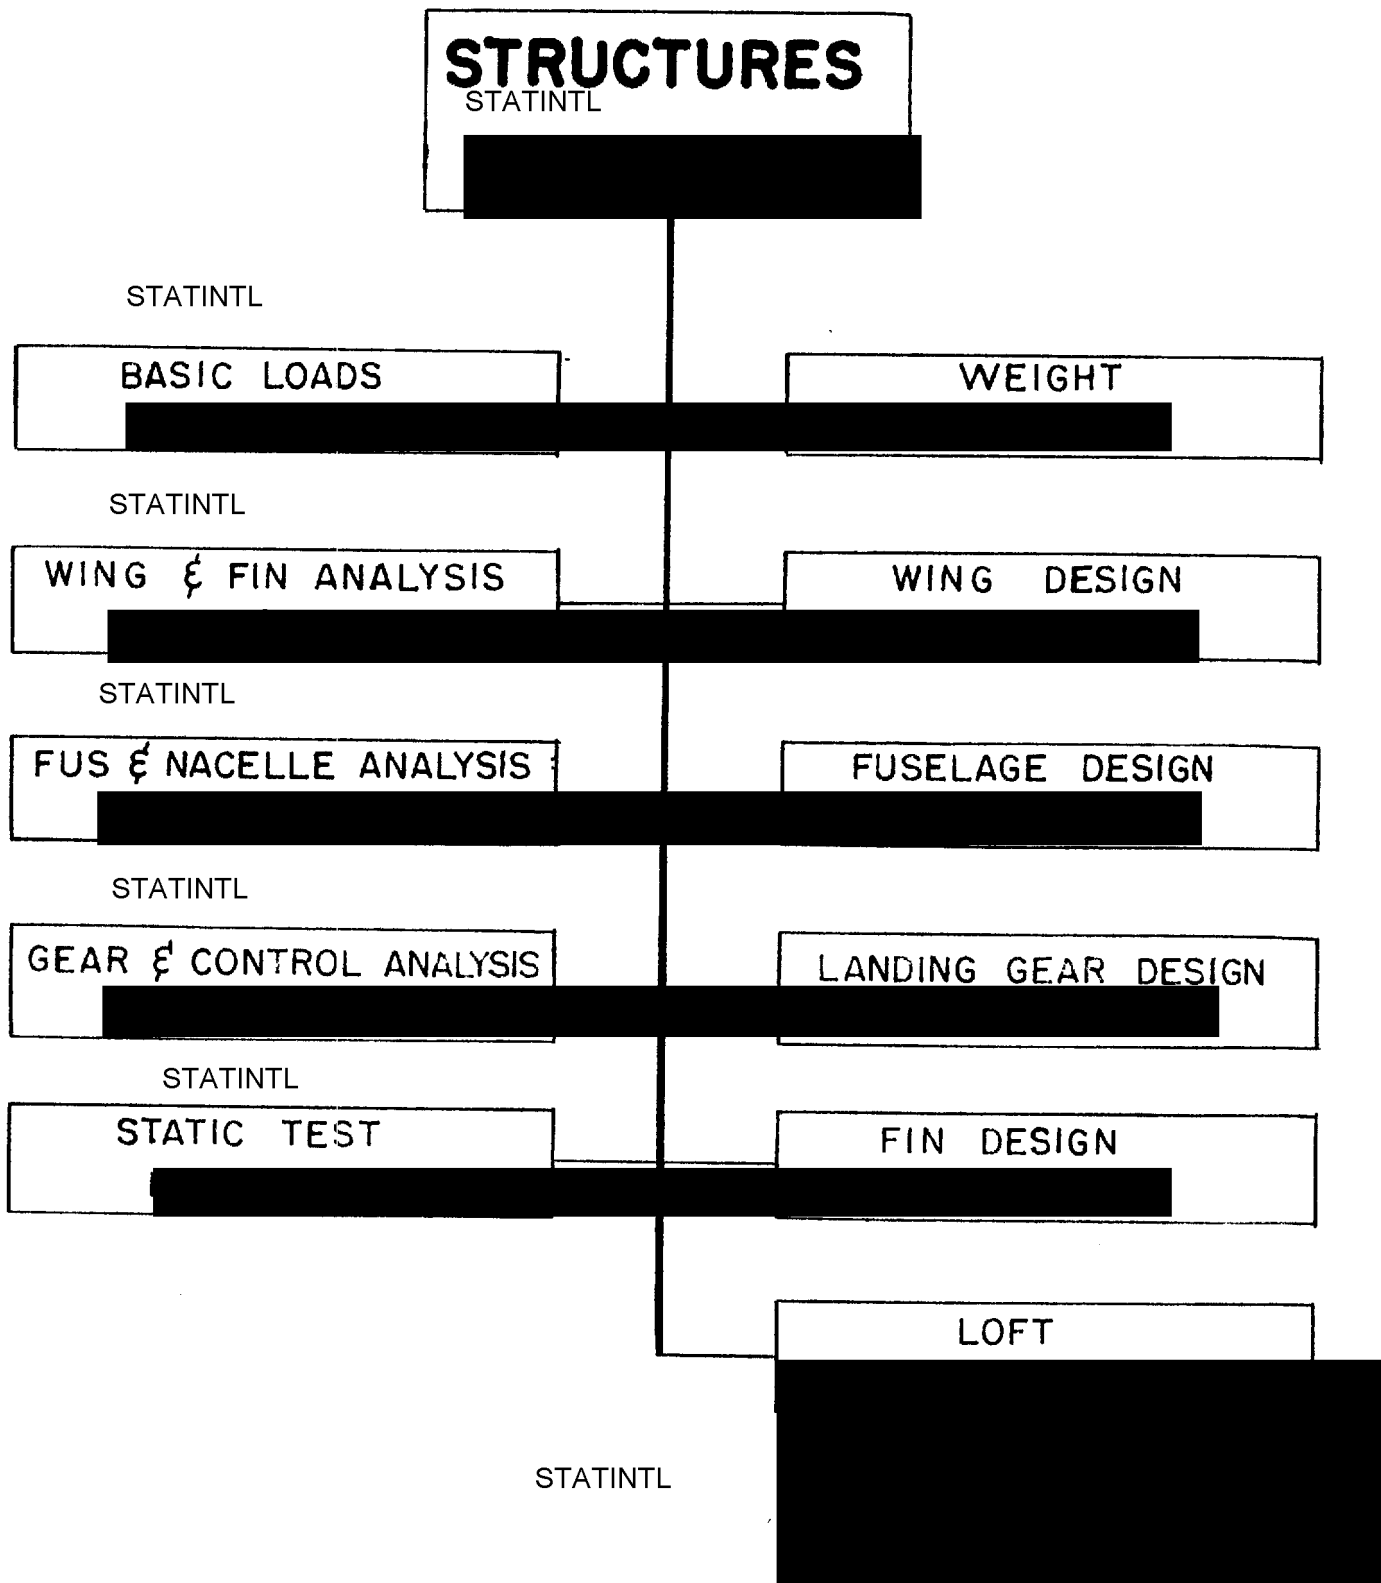

Clarence L. Johnson  
Vice President

Advanced Development Projects

# ADVANCED DEVELOPMENT PROJECTS

## ORGANIZATION CHART

SEPT. 21, 1959

### EQUIPMENT & SYSTEMS

STATINTL

STATINTL

POWER PLANT

SPECIAL EQUIPMENT

STATINTL

ESCAPE SYSTEM & COCKPIT

ELECTRICAL & RADIO

STATINTL

GROUND HANDLING EQUIP.

HYDRAULICS

STATINTL

CONTROLS

FUEL SYSTEM

STATINTL

AIR CONDITIONING

FUEL & HYD. TEST

INERTIAL GUIDANCE

STATINTL

Clarence L. Johnson  
Vice President

Advanced Development Projects

## ORGANIZATION CHART

SEPT. 21, 1959

STATINTL

**ENGINEERING  
U-2**

```
graph TD; A[ENGINEERING U-2] --- B[ ]; B --- C[PROJ. - [REDACTED]]; B --- D[ASST. PROJ. ENGINEER [REDACTED]]; C --- E[REDACTED]; D --- F[REDACTED];
```

STATINTL

PROJ. - [REDACTED]

ASST. PROJ. ENGINEER [REDACTED]


STATINTL

STATINTL


Clarence L. Johnson  
Vice President

# ADVANCED DEVELOPMENT PROJECTS ORGANIZATION CHART

SEPT. 21, 1959

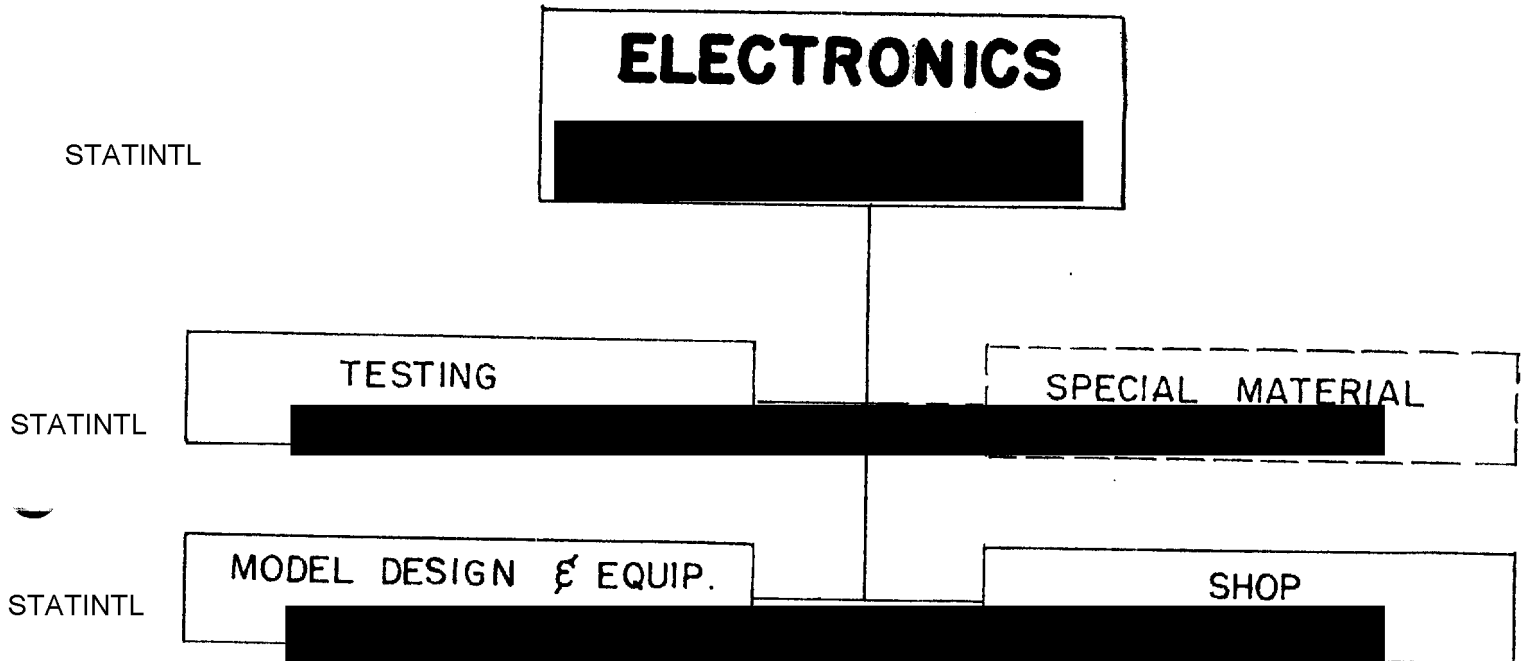

STATINTL



Clarence L. Johnson  
Vice President

## TEST PROGRAMS A-12

ITEM	WHERE TESTED	APPROX. TIME
LOW SPEED TUNNEL TESTS	L.A.C.	OCT.-NOV. 1959
HIGH SPEED TUNNEL TESTS	AMES-NASA	DEC. '59 / DEC. '60
FUEL TESTS-PHILLIPS PETROL.	P & W - L.A.C.	NOV.-DEC. 1959
FUEL SYSTEM TESTS	L.A.C.	DEC. '59 / JAN. '61
A.R. TESTS	STATINTL <span style="background-color: black; color: black;">████████</span> - L.A.C.	SEPT. 1959 →
TITANIUM FABRICATION PROBLEMS	L.A.C.	SEPT. '59 / JUNE '60
STATIC TESTS - TITANIUM STRUCT.	L.A.C.	OCT. '59 / NOV. '60
HYDRAULIC SYSTEM TESTS	L.A.C.	DEC. '59 / JAN. '61
INLET MODEL TESTS	L.A.C.-NASA	JAN. '60 / JAN. '61
TEMP. DISTRIBUTION MODEL	LANGLEY-NASA	FEB. 1960
LANDING GEAR DROP TESTS	L.A.C.	NOV.-DEC. 1960
